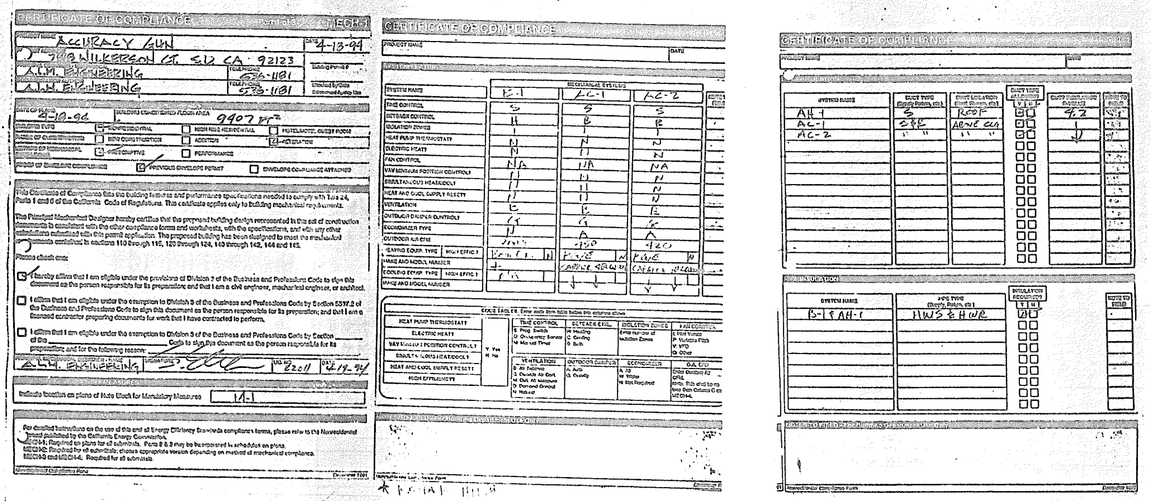

CERTIFICATE OF COMPLIANCE

PROJECT NAME: ACCURACY GUN — DATE: 4-13-94

ADDRESS: 7818 WILLERSON CT. SD CA 92123

A.L.M. ENGINEERING — TELEPHONE: 536-1181

A.L.M. ENGINEERING — TELEPHONE: 536-1181

DATE OF PLANS: 3-10-94 — BUILDING GROSS FLOOR AREA: 9407 ft²

BUILDING TYPE: NONRESIDENTIAL / NONRESIDENTIAL / HOTEL/MOTEL GUEST ROOM

PURPOSE OF CONSTRUCTION: NEW CONSTRUCTION / ADDITION / ALTERATION

METHOD OF MECHANICAL COMPLIANCE: PRESCRIPTIVE / PERFORMANCE

METHOD OF BUILDING COMPLIANCE: PREVIOUS ENVELOPE PERMIT / ENVELOPE COMPLIANCE ATTACHED

This Certificate of Compliance lists the building features and performance specifications needed to comply with Title 24, Parts 1 and 6 of the California Code of Regulations. This certificate applies only to building mechanical requirements.

The Planned Mechanical Designer hereby certifies that the proposed building design represented in this set of construction documents is consistent with the other compliance forms and worksheets, with the specifications, and with any other calculations submitted with this permit application. The proposed building has been designed to meet the mechanical requirements contained in sections 110 through 116, 120 through 124, 140 through 142, 144 and 145.

Please check one:

- I hereby affirm that I am eligible under the provisions of Division 3 of the Business and Professions Code to sign this document as the person responsible for its preparation and that I am a civil engineer, mechanical engineer, or architect.
- I affirm that I am eligible under the exemption to Division 3 of the Business and Professions Code by Section 5537.2 of the Business and Professions Code to sign this document as the person responsible for its preparation; and that I am a licensed contractor preparing documents for work that I have contracted to perform.
- I affirm that I am eligible under the exemption to Division 3 of the Business and Professions Code by Section ____ of the ____ Code to sign this document as the person responsible for its preparation and for the following reason: ____

PREPARER'S NAME: A.L.M. ENGINEERING — SIGNATURE: [signature] — LIC NO: 22011 — DATE: 4-13-94

Indicate location on plans of Note Block for Mandatory Measures: M-1

For detailed instructions on the use of this and all Energy Efficiency Standards compliance forms, please refer to the Nonresidential Manual published by the California Energy Commission.
§10-114: Required on plans for all submittals. Parts 6 & 9 may be incorporated in schedule on plans.
§10-116: Required for all submittals; choose appropriate version depending on method of mechanical compliance.
§10-116-3 and §10-116-4. Required for all submittals.

CERTIFICATE OF COMPLIANCE

PROJECT NAME: ____ — DATE: ____

SYSTEM NAME	RS-1	AC-1	AC-2
FAN CONTROL	S	S	S
OUTSIDE AIR CONTROL	H	E	E
ISOLATION DEVICE	I	I	I
HEAT PUMP THERMOSTATS	N	N	N
ELECTRIC HEATS	N	N	N
FAN CONTROL	NA	NA	NA
VAV/MULTI-ZONE POSITION CONTROLS	N	N	N
SIMULTANEOUS HEAT/COOL	N	N	N
HEAT AND COOL SUPPLY RESETS	N	N	N
VENTILATION	E	E	E
OUTDOOR CHECKER CONTROLS	G	G	G
ECONOMIZER TYPE	N	A	A
OUTDOOR AIR CFM	200	450	420
HEATING EQUIP. TYPE / HIGH EFFICIENCY	FURNACE / N	FURNACE / N	FURNACE / N
MAKE AND MODEL NUMBER	[illegible]	CARRIER 58AV	CARRIER 58AV
COOLING EQUIP. TYPE / HIGH EFFICIENCY	[illegible] / Y	[illegible] / Y	[illegible] / Y
MAKE AND MODEL NUMBER			

SYSTEM TYPES: Fill out this form below the entries above.

HEAT PUMP THERMOSTATS	Y, Yes / N, No	TIME CONTROL: 1 Prog. Switch; 2 On/Off/Prog Switch; 3 Mix Lat Timer	SETBACK CONTROL: 1 Heating; 2 Cooling; 3 Both	ISOLATION DEVICE: Enter number of Isolation Zones	FAN CONTROL: 1 Fixed Speed; 2 Variable Speed; 3 Other
ELECTRIC HEATS					
VAV/MULTI-ZONE POSITION CONTROLS					
SIMULTANEOUS HEAT/COOL					
HEAT AND COOL SUPPLY RESETS		VENTILATION: 1 Fixed; 2 Outside Air Econ; 3 Out. Air Monitor; 3 Demand Control; 4 Natural	OUTDOOR CHECKER: 1 Auto; 2 Manual	ECONOMIZER: A, Air; W, Water; N, Not Required	OA, CFM: Enter Outside Air CFM. Enter Min. Min and Max Flow Rate Ratio in Decimal.
HIGH EFFICIENCY					

CERTIFICATE OF COMPLIANCE

PROJECT NAME: ____ — DATE: ____

SYSTEM NAME	FAN TYPE (Supply, Return, etc.)	INSULATION LOCATION (Duct, Plenum, etc.)	DUCTS SEALED AT LEAKAGE LEVEL	SUPPLY DUCT LOCATION (Attic, Crawl, etc.)	RETURN DUCT LOCATION (Attic, Crawl, etc.)
AH-1	S	ROOF	3	4.2	N/A
AC-1	S&R	ABOVE CLG	1	1	1.3
AC-2	"	"	"	1	1.3

SYSTEM NAME	PIPE TYPE (Supply, Return, etc.)	INSULATION RESISTANCE TYPE 1	TYPE 2	NOTES TO BUILD
RS-1 & AH-1	HWS & HWR			

A.L.M. ENG.
536-1181

REVISIONS	BY

DRAWING CONTENTS: TITLE 24 ENERGY CALCS.

PROJECT: ACCURACY GUN — 7818 Willerson Ct. San Diego, CA 92123

- DESIGN DEVELOP.
- PLAN CHECK 1
- PLAN CHECK 2 — 5-16-94, 8-22-94
- BIDDING
- CONSTRUCTION
- CLARIFICATION
- RECORD

Date 4-18-94

Scale

Drawn

Job 9318

Sheet T24

Of 23 Sheets

24 X 36 PRINTED ON NO. 1000H CLEARPRINT

490
